WESTERN INSTITUTE OF TECHNOLOGY

College of Engineering

Information Technology Department

1st Semester A.Y. 2026-2027

ITPD4 - SOFTWARE ENGINEERING

PREFINAL EXAMINATION - TEST II

SYSTEM PROJECT DOCUMENTATION

Digi-Konek: Electronics-Focused Online Marketplace

Group Name: TechILO

Group Number: Pending confirmation

BSIT 3 - Section 1

Group Members

Patiño, Keith Erwin Mikhail G.

Peñas, Emmanuel Angelo

Balsomo, John Rey

Bolivar, Jaderick

Tan, Rainier Ryan

Submitted to:
Mohamed Mogib P. Elkordy
ITPD4 Instructor

Date Submitted: _____

TABLE OF CONTENTS

Section	Page
1. PROJECT PROFILE AND CONTINUITY	3
2. PROBLEM, USERS, AND PROJECT OBJECTIVES	4
3. SCOPE BASELINE AND IMPLEMENTED CORE FEATURES	5
4. UPDATED FEASIBILITY SUMMARY	6
5. WORK BREAKDOWN STRUCTURE AND RESPONSIBILITY MATRIX	7
5.1 Responsibility Matrix	8
6. PROJECT SCHEDULE / GANTT CHART AND MILESTONES	9
6.1 Milestones and Dependencies	10
7. SYSTEM DESIGN SUMMARY	11
7.2 Database / ERD	12
7.2 Database / ERD — Key Reference	13
7.3 Key UML / Workflow Diagram	14
7.4 Updated Interface / Screen Flow	15
8. IMPLEMENTED SYSTEM AND WORKING FEATURES	16
9. GITHUB REPOSITORY AND SOURCE-CODE EVIDENCE	17
10. BASIC FUNCTIONAL VERIFICATION / CURRENT SYSTEM STATUS	18
11. RISK REGISTER AND CURRENT RISK RESPONSES	19
12. VIDEO PRESENTATION AND MEMBER NARRATION RECORD	20
13. TEAM CONTRIBUTION RECORD	21
14. APPENDICES / SUPPORTING EVIDENCE	22
Appendix A - Additional System Screenshots	22
Appendix B - Updated Diagrams / Models	22
Appendix C - GitHub Commit / Contribution Evidence	22
Appendix D - Other Approved Supporting Evidence	22
Appendix D - Source Register and Reconciliation	23
FINAL SUBMISSION CHECKLIST	24
Team Certification	24

The report follows the approved Digi-Konek project through requirements, design, and the latest Week 8 planning baseline. Evidence-dependent implementation and submission entries are identified in their corresponding sections.

1. PROJECT PROFILE AND CONTINUITY

Field	Team Entry
Approved Project Title	Digi-Konek: Electronics-Focused Online Marketplace
Group Name / Number	TechILO / Pending confirmation
Section	BSIT 3 - Section 1
Target User / Client	Electronics Retailer, Electronics Supplier, System Administrator
Development Methodology	Agile development using Scrum
Current System Version / Build	Pending submission-build identification
GitHub Repository URL	Pending repository upload
Video URL / File Name	Pending recording and submission

1.1 Project Continuity Summary

Digi-Konek continues the approved B2B electronics marketplace developed through the project concept, methodology, requirements, analysis, design, and Week 8 planning materials. It addresses fragmented procurement through phone calls, messages, spreadsheets, websites, and supplier visits. Retailers browse and compare products and submit wholesale orders; suppliers maintain listings, stock, and received orders; administrators verify suppliers and oversee marketplace accounts.

The Prefinal phase carries these requirements into the established three-tier PHP/MySQL web architecture. The latest Week 8 package retains ten marketplace modules and a proposed 45-day implementation schedule. It does not establish completed implementation, instructor acceptance, or individual accomplishments.

1.2 Previous Outputs Reviewed

Previous Output	Review Record
Project Concept and Team Charter	Week 1 concept; Midterm portfolio team context
Methodology and Lifecycle Plan	Week 2; Agile/Scrum lifecycle
SRS / Requirements	Week 3; reconciled Midterm requirements
Use Cases / User Stories	Week 4 and Midterm portfolio
UML / Wireframes / Architecture / ERD	Weeks 5–6 and reconciled Midterm portfolio
Midterm Feedback	Actual instructor-feedback record remains pending in Week 8
Week 8 Planning Package	Latest revised 45-day version; controlling planning baseline

Source: S1–S5, S7 and S8; source register in Appendix D.

2. PROBLEM, USERS, AND PROJECT OBJECTIVES

2.1 Problem / Need Being Addressed

Electronics retailers need reliable access to computer components, input devices, and output devices. Product information, prices, availability, and supplier details are distributed across separate websites, messages, calls, spreadsheets, and face-to-face transactions. Retailers must gather and compare this information manually, while suppliers have limited visibility among potential business customers.

Digi-Konek provides a centralized marketplace for product discovery, supplier information, comparison, wholesale ordering, and order tracking. It supports the documented retailer-to-supplier process without taking responsibility for excluded payment, logistics, or after-sales services.

2.2 Target Users / Stakeholders

User / Stakeholder	Need / Role in the System
Electronics Retailer	Find and compare electronic products; manage a cart; place wholesale orders; monitor order status.
Electronics Supplier	Publish and maintain product information and stock; receive and process orders; view sales reports.
System Administrator	Review supplier documents, verify suppliers, manage accounts and product classifications, and review marketplace reports.

2.3 Approved Project Objectives

1. Provide a centralized B2B platform connecting electronics retailers and suppliers.

2. Help retailers browse, search, filter, and compare product information, prices, suppliers, and availability.

3. Enable suppliers to maintain product listings and inventory information.

4. Support shopping carts, wholesale order submission, supplier decisions, and retailer order tracking.

5. Support supplier verification, administrative oversight, notifications, reporting, and audit records.

Source: S1; S3; S4; S5; S7; S8. Objectives consolidate the documented purpose and requirements without adding scope.

3. SCOPE BASELINE AND IMPLEMENTED CORE FEATURES

The following is the retained scope baseline. “Verification pending” means the uploaded references do not establish a current demonstrated result; it does not mean the feature is absent from the application.

Classification	Feature / Requirement	Implementation Status	Evidence / Reference
IN SCOPE	Accounts, authentication, supplier verification and account/document controls	Verification pending	FR-01–03, 16, 18; WBS 2.0
IN SCOPE	Product listings, images/specifications, search, comparison, categories and brands	Verification pending	FR-04–08, 17; WBS 3.0
IN SCOPE	Cart quantities, wholesale orders, supplier decisions and tracking	Verification pending	FR-09–10, 12–13; WBS 4.0
IN SCOPE	Stock checks and inventory updates without negative quantities	Verification pending	FR-14; WBS 3.0–4.0
IN SCOPE	Notifications, supplier/marketplace reports and audit records	Verification pending	FR-11, 15, 19–20; WBS 5.0–6.0
OUT OF SCOPE	Delivery/logistics, warehouse management, online payments, lending and accounting integration	Excluded from baseline	Week 8 scope; Weeks 1–4
OUT OF SCOPE	Installation, repairs and warranty claims	Excluded from baseline	Week 8 scope; Weeks 1–4

3.1 Core Features Demonstrated in Test II

The final demonstration record is pending. Week 8 establishes the following core implementation priorities, to be confirmed against the submitted build:

1. MySQL schema and authenticated retailer, supplier, and administrator access.
2. Supplier verification, document access checks, and product publication controls.
3. Catalog, categories/brands, stock display, search, comparison, and cart quantities.
4. Pending orders, supplier processing, stock updates, and retailer status tracking.
5. Ordering notifications and audit events, followed by reports and quality checks.

Source: S8 scope and Appendix G traceability; S7 functional requirements. No approved core requirement is silently reclassified as a future enhancement.

4. UPDATED FEASIBILITY SUMMARY

The latest Week 8 decision remains the documented feasibility baseline. A new assessment or approval is not asserted without additional evidence.

Feasibility Area	Current Finding / Evidence	Decision
Technical	The PHP/MySQL web stack matches the Week 2 plan and the established three-tier design. Implementation and integration still require testing.	Feasible
Operational	Retailer ordering, supplier processing, and administrator verification follow the documented workflow. Real-user usability evidence is still needed.	Needs Revision
Economic	A local academic demonstration is the proposed baseline. Equipment, connectivity, and any PHP/MySQL hosting costs must be confirmed.	Needs Revision
Schedule	The proposed 45-day plan needs 240 person-hours plus 48 contingency hours. Five members must confirm part-time availability.	Needs Revision
Legal	Supplier documents, user accounts, and product images require access restrictions, permission, and retention decisions. Use synthetic demonstration data.	Needs Revision
Organizational	TechILO has a documented representative and roster. Client participation, review attendance, and individual work commitments need confirmation.	Needs Revision

Overall Feasibility Decision

Needs Revision

The documented PHP/MySQL architecture is suitable for an academic implementation. However, WBS 1.0 must confirm instructor feedback, acceptance targets, team capacity, available resources, and data permissions. The 45-day schedule and 288-person-hour allowance remain proposed estimates, not verified delivery capacity or a guarantee of production readiness.

Source: S8, Updated Feasibility Study and Final Team Justification. This later decision supersedes the earlier feasibility conclusion in the Midterm materials.

5. WORK BREAKDOWN STRUCTURE AND RESPONSIBILITY MATRIX

Owners and work packages follow the latest Week 8 assignments. Ownership is proposed; actual completion and member acceptance require evidence.

WBS Code	Task / Work Package	Owner	Expected Output	Status
1.0	Planning and design reconciliation	Patiño	Reconciled backlog, scope, ERD/interfaces, and dated review record.	Pending verification
2.0	Database, authentication, and supplier verification	Balsomo	Schema plus passing login, role, and supplier-verification checks.	Pending verification
3.0	Product catalog and inventory interfaces	Bolivar	Catalog and stock interfaces pass role and product checks.	Pending verification
4.0	Shopping cart and order processing	Peñas	Order flow rejects insufficient stock and repeated processing.	Pending verification
5.0	Notifications, reporting, and audit	Tan	Notification/report/audit outputs reconcile to seeded orders.	Pending verification
6.0	End-to-end integration	Patiño	Integrated demonstration with traceable test and defect records.	Pending verification
7.0	System testing and revisions	Tan	Test report, resolved critical defects, and documented remaining limits.	Pending verification
8.0	Deployment and handover	Patiño	Reproducible deployment, smoke test, guide, backup, and demo evidence.	Pending verification

Source: S8, Work Breakdown Structure. Completion status is not inferred from elapsed calendar dates.

5.1 Responsibility Matrix

Task / Deliverable	Responsible Member	Support Member	Reviewer	Evidence
1.0 Planning and design reconciliation	Patiño	Bolivar	Tan	Planned: Reconciled backlog, scope, ERD/interfaces, and dated review record.
2.0 Database, authentication, and supplier verification	Balsomo	Peñas	Patiño	Planned: Schema plus passing login, role, and supplier-verification checks.
3.0 Product catalog and inventory interfaces	Bolivar	Peñas, Balsomo	Tan	Planned: Catalog and stock interfaces pass role and product checks.
4.0 Shopping cart and order processing	Peñas	Patiño, Balsomo, Bolivar, Tan	Balsomo	Planned: Order flow rejects insufficient stock and repeated processing.
5.0 Notifications, reporting, and audit	Tan	Patiño	Peñas	Planned: Notification/report/audit outputs reconcile to seeded orders.
6.0 End-to-end integration	Patiño	Balsomo, Bolivar, Tan	Peñas	Planned: Integrated demonstration with traceable test and defect records.
7.0 System testing and revisions	Tan	All members	Patiño	Planned: Test report, resolved critical defects, and documented remaining limits.
8.0 Deployment and handover	Patiño	Peñas, Tan	Balsomo	Planned: Reproducible deployment, smoke test, guide, backup, and demo evidence.

A task is considered Done under the Week 8 reporting rules only when acceptance evidence and reviewer sign-off are attached. Proposed assignments are not a substitute for the actual contribution record in Section 13.

Source: S8, Responsibility Matrix and Weekly Progress-Reporting Rules.

6. PROJECT SCHEDULE / GANTT CHART AND MILESTONES

The controlling proposed schedule spans September 14–October 28, 2026: 45 inclusive calendar days (1.5 months using a 30-day planning month). Work packages run sequentially. The dates require team and course-calendar confirmation; no actual completion dates are established.

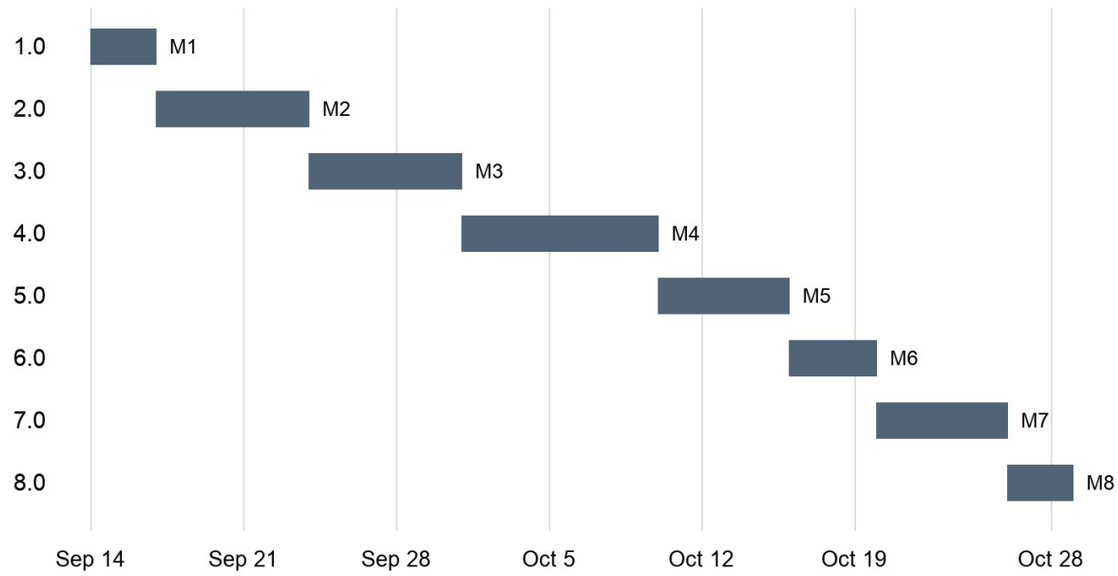


Figure 1. Proposed Week 8 Gantt chart. M1–M8 identify the target milestones; bars do not indicate actual progress.

Task	Owner	Start	End	Dependency
1.0 Planning and design reconciliation	Patiño	09/14/2026	09/16/2026	None; review access required
2.0 Database, authentication, and supplier verification	Balsomo	09/17/2026	09/23/2026	1.0 completed
3.0 Product catalog and inventory interfaces	Bolivar	09/24/2026	09/30/2026	2.0 completed
4.0 Shopping cart and order processing	Peñas	10/01/2026	10/09/2026	3.0 completed
5.0 Notifications, reporting, and audit	Tan	10/10/2026	10/15/2026	4.0 completed
6.0 End-to-end integration	Patiño	10/16/2026	10/19/2026	5.0 completed
7.0 System testing and revisions	Tan	10/20/2026	10/25/2026	6.0 completed
8.0 Deployment and handover	Patiño	10/26/2026	10/28/2026	7.0 completed

Duration allocation: 3 + 7 + 7 + 9 + 6 + 4 + 6 + 3 = 45 days. Baseline effort is 240 person-hours plus 48 contingency hours (288 total). The 48 contingency hours must fit within the schedule. The proposed capacity assumption is five members averaging 10 hours/week for six full weeks; availability and peak-week allocation remain unconfirmed.

Source: S8, Effort Estimates, Project Schedule, and Appendix A.

6.1 Milestones and Dependencies

No.	Milestone / Checkpoint	Dependency / Prerequisite	Target / Actual Date	Status
1	M1: Reconciled backlog, scope, ERD/interfaces, and dated review record.	1.0 completed; prerequisites: None; review access required	09/16/2026 / Actual: pending	Pending verification
2	M2: Schema plus passing login, role, and supplier-verification checks.	2.0 completed; prerequisites: 1.0 completed	09/23/2026 / Actual: pending	Pending verification
3	M3: Catalog and stock interfaces pass role and product checks.	3.0 completed; prerequisites: 2.0 completed	09/30/2026 / Actual: pending	Pending verification
4	M4: Order flow rejects insufficient stock and repeated processing.	4.0 completed; prerequisites: 3.0 completed	10/09/2026 / Actual: pending	Pending verification
5	M5: Notification/report/audit outputs reconcile to seeded orders.	5.0 completed; prerequisites: 4.0 completed	10/15/2026 / Actual: pending	Pending verification
6	M6: Integrated demonstration with traceable test and defect records.	6.0 completed; prerequisites: 5.0 completed	10/19/2026 / Actual: pending	Pending verification
7	M7: Test report, resolved critical defects, and documented remaining limits.	7.0 completed; prerequisites: 6.0 completed	10/25/2026 / Actual: pending	Pending verification
8	M8: Reproducible deployment, smoke test, guide, backup, and demo evidence.	8.0 completed; prerequisites: 7.0 completed	10/28/2026 / Actual: pending	Pending verification

WBS 1.0 closes planning/design revisions. WBS 2.0–3.0 continue Sprint 3; WBS 4.0–6.0 continue Sprint 4; WBS 7.0–8.0 continue Sprint 5. The source does not establish these dates as the official submission deadline.

Source: S8, Milestones and Dependencies; S2 lifecycle plan.

7. SYSTEM DESIGN SUMMARY

7.1 System Architecture

The documented design is a three-tier layered web application. HTML, CSS, and JavaScript provide role-specific interfaces. Modular PHP business logic handles marketplace operations, and the data-access layer persists structured records in MySQL. The current approved design requires no external payment, logistics, or third-party notification service.

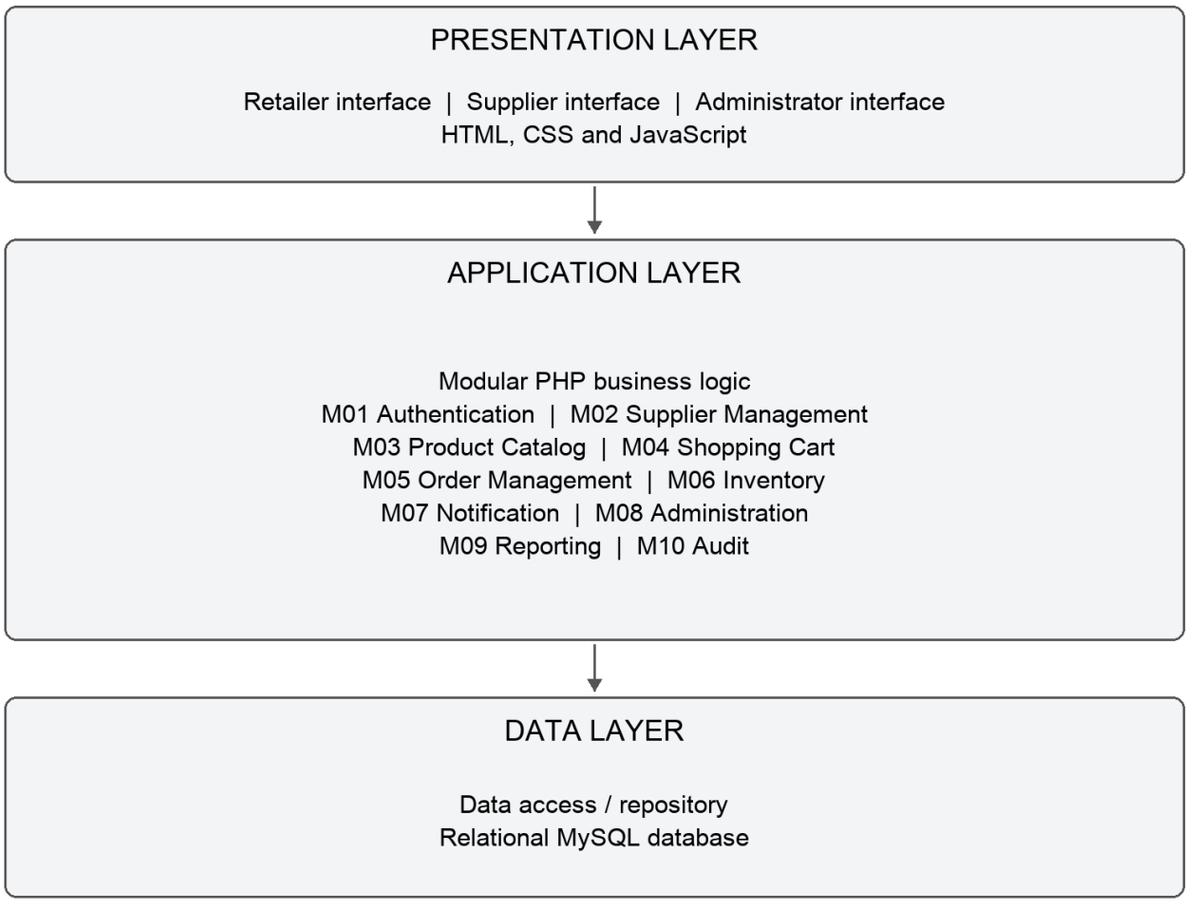


Figure 2. Three-tier architecture redrawn from the Midterm architecture and module list.

Separation of presentation, business logic, and persistence supports maintainability and testing. Authentication, role controls, validation, transactions, referential integrity, and audit records support the documented security and reliability goals. These are design responsibilities, not proof of tested quality targets.

Source: S5, Software Architecture and Module Design; S7, G.1–G.8.

7.2 Database / ERD

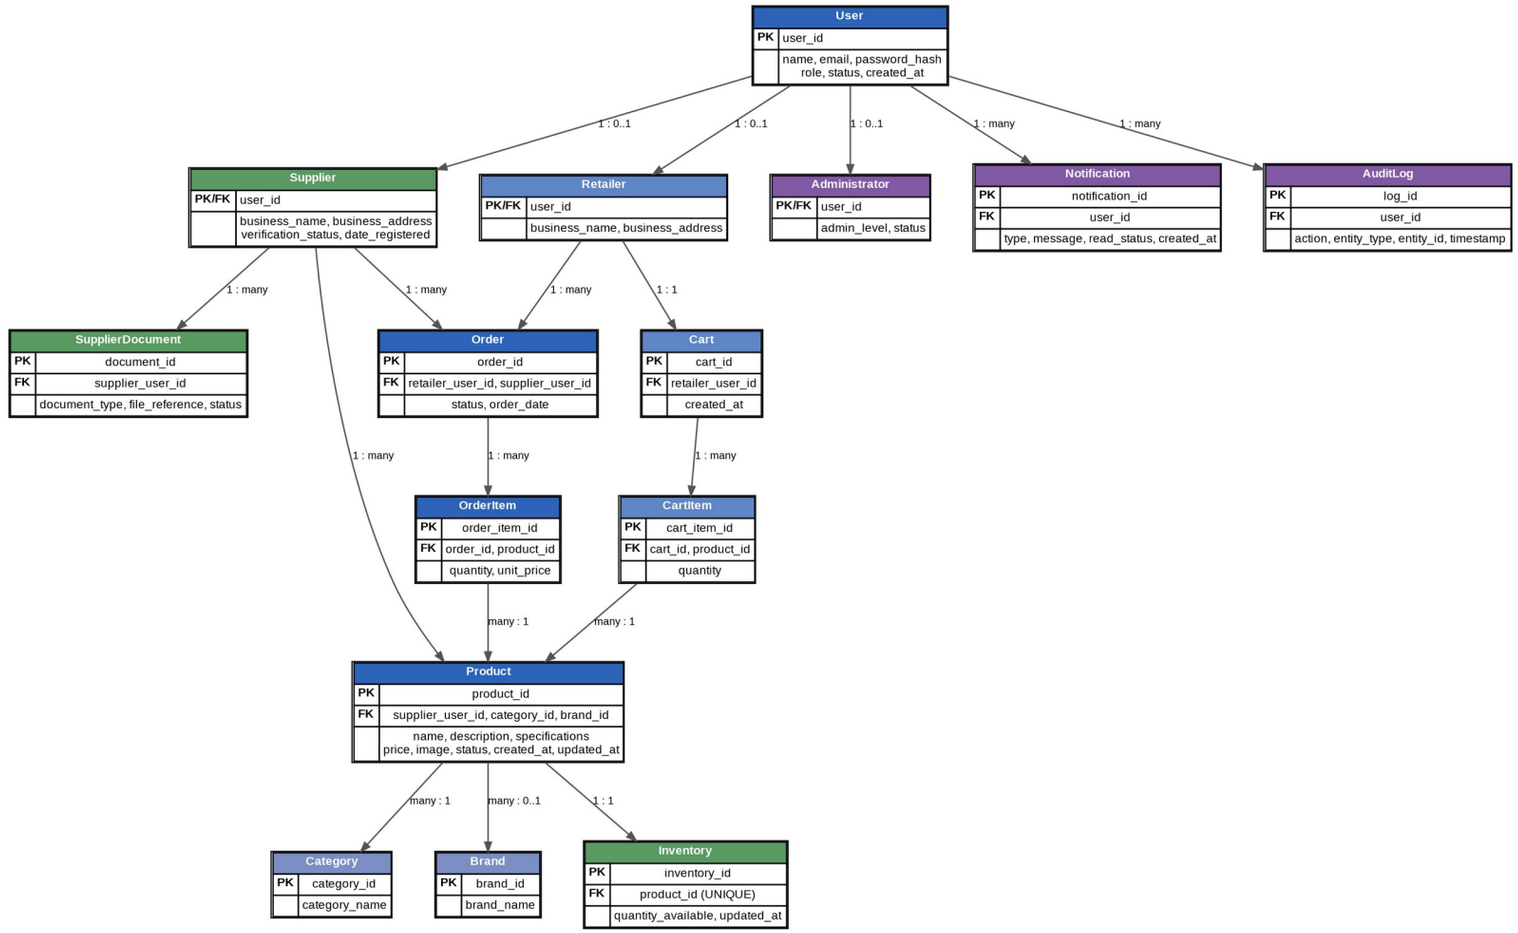


Figure 3. Reconciled ERD reproduced from the Midterm portfolio, Section G.12; shared profile identities retained by Week 8.

Source: S7, G.10–G.12; S8, Appendix E.

7.2 Database / ERD — Key Reference

The reconciled design shares User.user_id as the primary/foreign key of Supplier, Retailer, and Administrator. Week 8 retains this identity rule. Validation against the submission schema remains pending.

Entity	Primary Key	Foreign Key / Relationship
User	user_id	—
Supplier	user_id	user_id → User.user_id
Retailer	user_id	user_id → User.user_id
Administrator	user_id	user_id → User.user_id
SupplierDocument	document_id	supplier_user_id → Supplier.user_id
Category	category_id	—
Brand	brand_id	—
Product	product_id	supplier_user_id, category_id, brand_id
Inventory	inventory_id	product_id → Product.product_id (unique)
Cart	cart_id	retailer_user_id → Retailer.user_id
CartItem	cart_item_id	cart_id, product_id
Order	order_id	retailer_user_id, supplier_user_id
OrderItem	order_item_id	order_id, product_id
Notification	notification_id	user_id → User.user_id
AuditLog	log_id	user_id → User.user_id

Products belong to one category; suppliers may own many products and submit multiple documents. Retailers place orders with suppliers. Orders contain order items; carts contain cart items. Notifications and audit logs reference the responsible or receiving user. The key reference explains the source ERD and is not an exported live schema.

Source: S7, entity/key analysis and relationship table; S8 shared-identity reconciliation.

7.3 Key UML / Workflow Diagram

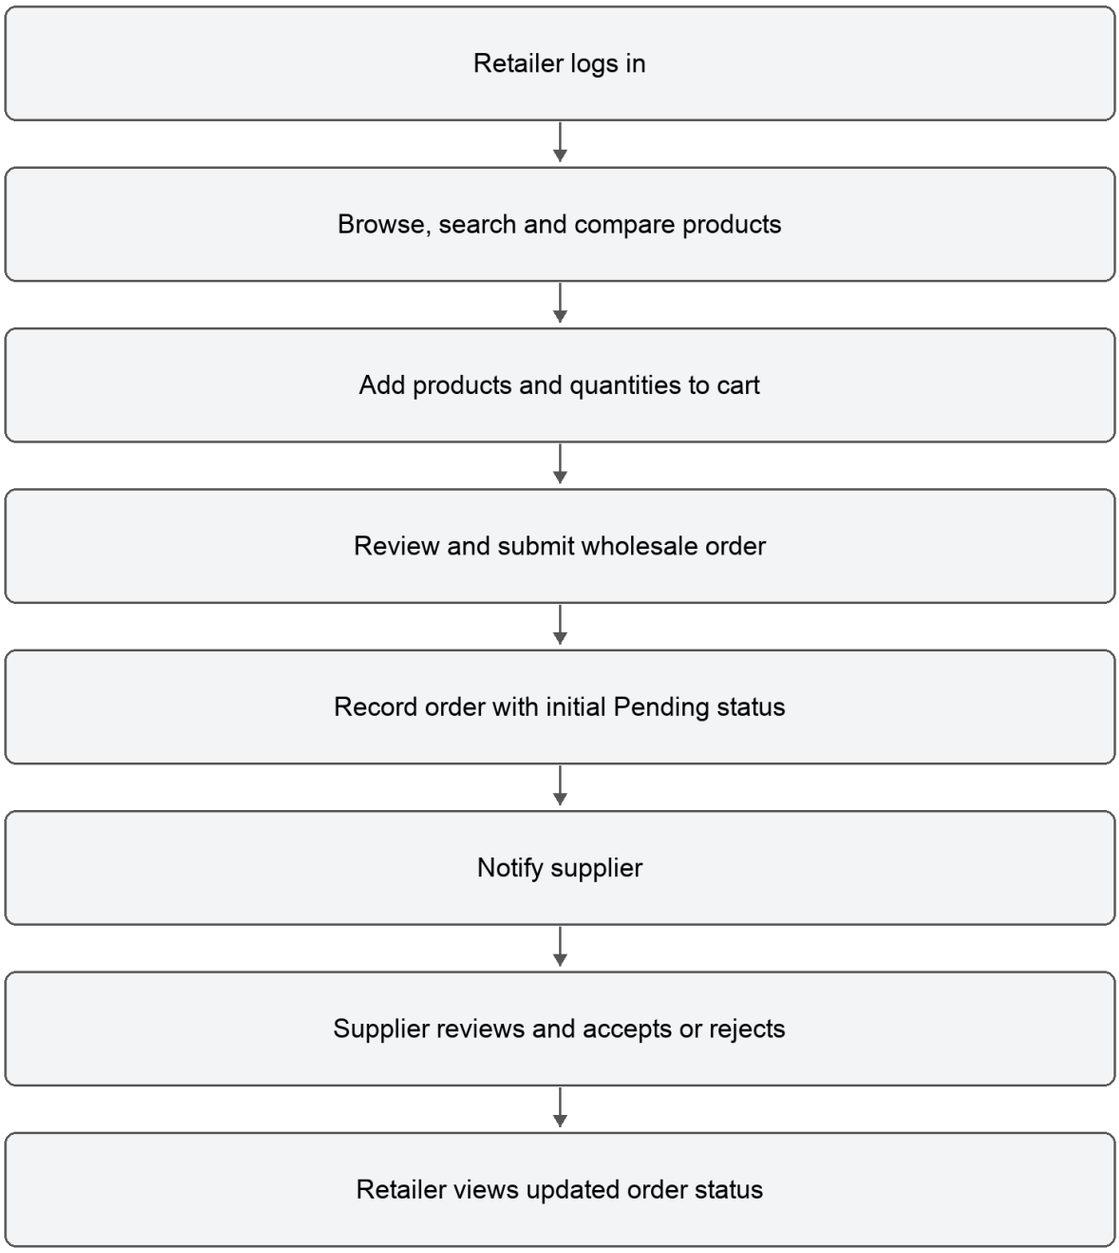


Figure 4. Retailer-to-supplier workflow redrawn from Week 4 To-Be analysis and the later Place Order / Process Order descriptions.

The design connects cart, order, inventory, notification, and audit responsibilities. Week 8 leaves exact order-state transitions and inventory-update timing for reconciliation; this figure therefore preserves only the supported high-level sequence. It does not add cancellation, payment, delivery, or other unsupported processing steps.

Source: S4, Proposed To-Be Process; S5 sequence descriptions; S7 navigation flow; S8 pending order-state decisions.

7.4 Updated Interface / Screen Flow

The latest supplied interface flow covers the following user journeys. The Week 8 package identifies updated wireframes and a recorded usability walkthrough as pending; these flows remain reference design, not working-system screenshots.

Workflow / Use Case	Starting Screen	Key Screens in Order	Expected End State
Register Account	Login / Landing Screen	Register Account → Registration Form → Account Confirmation	User account registered; user can proceed to login.
Authenticate User	Login Screen	Login Form → Credential Validation → Role-Based Dashboard	Authenticated and redirected to the appropriate dashboard.
Search Products	Retailer Dashboard	Product Catalog → Search/Filter → Search Results → Product Details	Matching products displayed based on criteria.
Compare Products	Product Search Results	Select Products → Compare Products → Comparison Results	Selected products displayed side-by-side.
Place Order	Product Details / Shopping Cart	Add to Cart → Shopping Cart → Order Review → Order Confirmation	Wholesale order submitted with Pending status.
Manage Products	Supplier Dashboard	Products → Add/Edit Product → Product Information → Save Confirmation	Supplier listing created or updated.
Process Order	Supplier Dashboard	Orders → Order Details → Accept/Reject Order → Status Confirmation	Order status updated based on decision.
Track Order	Retailer Dashboard	My Orders → Order Details → Order Status	Retailer views current order status.
Verify Supplier	Administrator Dashboard	Supplier Verification → Supplier Details → Documents → Approve/Reject → Confirmation	Supplier verification status updated.
Generate Sales Report	Supplier Dashboard	Sales Reports → Report Filters → Report Results	Supplier views generated sales report.

Source: S7, F.4 Navigation Flow; S5 navigation table; S8, Appendix D.

8. IMPLEMENTED SYSTEM AND WORKING FEATURES

This section retains the approved module responsibilities and Week 8 ownership. The uploaded planning/design documents do not verify a current software build. Each working-status entry therefore remains pending evidence instead of presenting the design as a demonstrated result.

Module / Feature	What It Does	Primary Member	Status	Screenshot / Evidence
M01 Authentication Module	Registration, login, authentication, role control	Balsomo (proposed)	Verification pending	Pending actual-system evidence
M02 Supplier Management Module	Supplier verification and supplier profile management	Balsomo (proposed)	Verification pending	Pending actual-system evidence
M03 Product Catalog Module	Product listing, browsing, searching, filtering, comparison	Bolivar (proposed)	Verification pending	Pending actual-system evidence
M04 Shopping Cart Module	Maintain selected retailer products	Peñas (proposed)	Verification pending	Pending actual-system evidence
M05 Order Management Module	Create and process wholesale orders	Peñas (proposed)	Verification pending	Pending actual-system evidence
M06 Inventory Module	Maintain and update stock quantities	Bolivar / Peñas (proposed)	Verification pending	Pending actual-system evidence
M07 Notification Module	Generate important system/order notifications	Tan (proposed)	Verification pending	Pending actual-system evidence
M08 Administration Module	User, category, brand, and marketplace administration	Balsomo / Bolivar (proposed)	Verification pending	Pending actual-system evidence
M09 Reporting Module	Supplier and marketplace reports	Tan (proposed)	Verification pending	Pending actual-system evidence
M10 Audit Module	Record important marketplace activities	Tan (proposed)	Verification pending	Pending actual-system evidence

Source: S7, G.4 Module List; S8 WBS 2.0–5.0. Assignments show planning responsibility, not individual implementation credit.

8.1 System Screenshots

Actual working-system screenshots are pending. The supplied wireframes must not be labeled as implemented screens. Appendix A identifies the evidence needed for the approved flows; screenshots should be captioned and tied to the final build.

9. GITHUB REPOSITORY AND SOURCE-CODE EVIDENCE

Repository Information	Team Entry
GitHub Repository Name	Pending upload
Repository URL	Pending upload
Default / Submission Branch	Pending identification
Latest Submission Commit ID / Hash	Pending submission commit
README Included	Pending repository verification
Database / Setup Files Included	Pending repository verification
Source Code ZIP Submitted to GClass	Pending submission

9.1 Repository Structure / Selected Code Evidence

Repository-tree and representative code screenshots are pending. The evidence must correspond to the same version described in this report and demonstrated in the video. Only selected implementation evidence belongs in the printed package; the complete source belongs in GitHub and the required ZIP.

The repository must contain organized source files, the README, and database schema/migration/setup files. Private credentials must not be published. Meaningful existing development history should be preserved; unsupported historical commits or member contributions must not be fabricated.

Required source ZIP filename: ITPD4_TestII_TechILO_Digi-Konek_SourceCode.zip

Source: S0, Sections B and D; S8, Appendix F. Repository upload is pending.

10. BASIC FUNCTIONAL VERIFICATION / CURRENT SYSTEM STATUS

Expected results below come from the documented requirements and Week 8 acceptance groups. No execution result is invented from a planned test. Actual results and evidence must be entered for the submission build.

No.	Feature / Flow Checked	Expected Result	Actual Result / Status	Evidence
1	Registration and login	Required information validated; duplicate/incomplete input rejected; protected access authenticated.	Execution not established	Pending; TC-02
2	Supplier verification	Administrator reviews documents; unverified supplier cannot publish products.	Execution not established	Pending; TC-02
3	Catalog and product management	Authorized product maintenance; accurate filters and comparison results.	Execution not established	Pending; TC-03
4	Cart and wholesale order	Quantities validated; order/items recorded with initial Pending status.	Execution not established	Pending; TC-04
5	Supplier decision and stock	Accept/reject and tracking work; stock remains nonnegative; duplicate operations checked.	Execution not established	Pending; TC-04
6	Notifications, reports and audit	Order events notify users; date-filtered totals reconcile; activity is recorded.	Execution not established	Pending; TC-05
7	Quality and resilience	Browser/UI, access, input, load/availability criteria and backup/restore checked.	Execution not established	Pending; TC-07

Known Limitations / Pending Work

1. Week 8 leaves the NFR-05 availability target and measurement period unresolved (99.99% versus 99% in earlier requirements).

2. Password-storage wording, missing main-table requirement rows, and acceptance criteria require reconciliation.

3. Administrator provisioning, exact order-state transitions, and product deletion/history rules require confirmation.

4. Actual usability, load, browser, backup/restore, deployment, and current-build verification evidence remain to be recorded.

Source: S7 acceptance criteria; S8 findings and Appendix G. TC identifiers are planned test groups, not passing test results.

11. RISK REGISTER AND CURRENT RISK RESPONSES

The latest Week 8 register keeps six risks Open. No subsequent verified closure is established. The table preserves those statuses; controls are planned responses.

Risk ID	Risk Description	Probability / Impact	Mitigation / Contingency	Owner / Status
R-01	Feedback or unresolved SRS/design conflicts may change the implementation baseline.	Medium / High	Resolve WBS 1.0 findings; log changes and re-estimate affected tasks.	Patiño / Open
R-02	Competing orders or repeated supplier actions may oversell stock or duplicate orders.	Medium / High	Use atomic stock checks, valid state transitions, and duplicate-request tests in 4.0 and 7.0.	Peñas / Open
R-03	Unauthorized access or unsafe uploads may expose user or supplier documents.	Medium / High	Enforce role/ownership checks, upload validation, protected storage, and security tests.	Balsomo / Open
R-04	Member availability or integration complexity may exceed the proposed 45-day capacity.	High / High	Confirm availability, review progress weekly, and use the 48-hour contingency allowance.	Patiño / Open
R-05	Users may find product discovery or order actions confusing.	Medium / Medium	Run a recorded retailer/supplier walkthrough with synthetic data; revise and retest.	Bolivar / Open
R-06	Environment failure or a bad change may interrupt the demo or lose test data.	Medium / High	Version code/schema, back up MySQL data, and test restoration before deployment.	Tan / Open

Current Response Priorities

R-04 is Critical; R-01, R-02, R-03, and R-06 are High; R-05 is Medium. Scope/feedback conflicts require a reviewed change record. Inventory problems require reproduction and retesting. Access incidents require containment and credential review. Schedule pressure requires reassignment and the planned contingency allowance. Environment failures require restoration from a verified backup and smoke testing.

Week 8 proposes Friday progress reviews and immediate escalation of dependency, security, or data-loss blockers to Patiño. Other blockers are to be escalated within 48 hours. Meeting attendance, decisions, actual hours, evidence, and review outcomes still need to be recorded.

Source: S8, Risk Register, Risk Response Plan, and Weekly Progress-Reporting Rules.

12. VIDEO PRESENTATION AND MEMBER NARRATION RECORD

Every member must narrate a meaningful part of the actual project. The name should be stated or displayed at the beginning of that segment. The Week 8 assignments below are a planning reference; actual recorded topics and timestamps remain pending.

No.	Member Name	Role / Module	Video Segment / Topic Explained	Time Stamp
1	Patiño, Keith Erwin Mikhail G.	Group Representative / Integration Lead (proposed)	Pending recorded segment	Pending
2	Peñas, Emmanuel Angelo	Cart and Order Developer (proposed)	Pending recorded segment	Pending
3	Balsomo, John Rey	Database and Access Developer (proposed)	Pending recorded segment	Pending
4	Bolivar, Jaderick	Catalog / UI Developer (proposed)	Pending recorded segment	Pending
5	Tan, Rainier Ryan	Reporting / QA Coordinator (proposed)	Pending recorded segment	Pending

Video Link / File Name: Pending recording.
Required uploaded filename: ITPD4_TestII_TechILO_Digi-Konek_Video.mp4

Required Video Coverage

1. Opening: project title, group name/number, section, and complete member names.
2. Overview: problem, target users, and purpose.
3. Scope: implemented core features and approved deferred enhancements.
4. Actual-system demonstration of important user flows using realistic sample data.
5. Technical explanation of architecture, database, tools, and connections.
6. Each member’s own module, contribution, or responsibility.
7. GitHub structure and selected implementation evidence.
8. Current status, known limitations, and next implementation/testing work.

Source: S0, Section C and documentation Section 12; S8 proposed roles.

13. TEAM CONTRIBUTION RECORD

The current roster contains five members. Actual Prefinal contributions must be stated and confirmed by each member before signing. Week 8 identifies proposed assignments only; earlier-week contributions are not automatically carried forward as current accomplishments.

No.	Complete Name	Primary Role	Actual Contribution / Deliverables	Signature
1	Patiño, Keith Erwin Mikhail G.	Group Representative / Integration Lead (proposed)	Pending member confirmation of actual work and evidence.	_____
2	Peñas, Emmanuel Angelo	Cart and Order Developer (proposed)	Pending member confirmation of actual work and evidence.	_____
3	Balsomo, John Rey	Database and Access Developer (proposed)	Pending member confirmation of actual work and evidence.	_____
4	Bolivar, Jaderick	Catalog / UI Developer (proposed)	Pending member confirmation of actual work and evidence.	_____
5	Tan, Rainier Ryan	Reporting / QA Coordinator (proposed)	Pending member confirmation of actual work and evidence.	_____

Confirmation should identify specific system, documentation, repository, testing, or presentation outputs. A signature confirms the accuracy of the contribution statement; signatures are left blank for the members.

Source: S8, Team Contribution Record; S0, documentation Section 13.

14. APPENDICES / SUPPORTING EVIDENCE

Appendix A - Additional System Screenshots

Pending actual-system evidence. The supplied materials contain design wireframes, not verified Prefinal application screenshots. Capture only the submitted version and label the actor, feature, and result.

Evidence Area	Source-Based Flow to Show
Access and verification	Login/role access; supplier-document review and publication control.
Catalog	Supplier product maintenance; retailer browse/search/compare.
Transactions	Cart, Pending order, supplier decision, stock consistency, and retailer tracking.
Oversight	Notifications, supplier/marketplace reports, and audit records.

Appendix B - Updated Diagrams / Models

Figures 2–4 in Section 7 present the documented architecture, reconciled ERD, and core workflow. Section 7.4 records the supplied screen flow. They explain the reference design; matching them to the final submission build remains pending as required by Week 8.

Appendix C - GitHub Commit / Contribution Evidence

Pending repository upload, final commit identification, and verified member contribution evidence. The source ZIP, video, and report must use the same submitted version.

Appendix D - Other Approved Supporting Evidence

The following source register identifies the documents used. Later-week decisions control conflicts. The Midterm portfolio is used as the consolidation of Weeks 1–6; a separate Week 7 file was not supplied. S0 controls the required Prefinal format.

Appendix D - Source Register and Reconciliation

ID	Document	Use
S0	ITPD4 Prefinal.pdf	Official format, section order, submission and evidence requirements.
S1	Week 1 - Project Concept Paper.pdf	Project concept, procurement problem, initial scope and exclusions.
S2	Week 2.pdf	Agile/Scrum lifecycle, technology stack and change process.
S3	Week 3.pdf	Elicitation, initial SRS, requirements and traceability.
S4	Week 4.pdf	As-Is/To-Be process, actors, use cases and user stories.
S5	ITPD4_Weeks5-6_BSIT3-Section1_TechILO__Digi-Konek.pdf	UML, wireframes, architecture, modules, interfaces and data design.
S7	ITPD4_Midterm_Project_TechILO_Digi-Konek.docx	Consolidated Weeks 1–6 portfolio; reconciled module and identity models.
S8	ITPD4_Week8_ProjectPlanning_TechILO.docx (latest revised version)	Controlling roster, feasibility, proposed assignments, 45-day schedule, risks and pending confirmations.

Reconciliation Record

Conflict / Issue	Controlling Treatment
Six-member earlier roster versus five-member Week 8 roster	Use five members from Week 8; retain Emmanuel Angelo and Keith Erwin Mikhail G. spellings.
Earlier feasibility conclusions	Retain Week 8 overall decision: Needs Revision.
Earlier timelines and initial role labels	Use the revised September 14–October 28, 2026 schedule and proposed Week 8 responsibilities.
Availability, password wording and missing requirement rows	Retain Week 8 pending reconciliation; do not silently select an unsupported acceptance target.
Design versus actual implementation	Do not treat wireframes, planned tests, assignments, or dates as execution evidence.

FINAL SUBMISSION CHECKLIST

Complete the evidence-dependent checks before submission and printing. Items marked Pending require confirmation; they are not certified by the planning documents.

Requirement	Status
Long bond paper (8.5 × 13 inches)	Document configured; physical print pending
Required section order and Table of Contents	Included; final page references checked after rendering
Same approved semester project	Digi-Konek retained
Approved core features accurately represented	Baseline included; final implementation verification pending
Video matches GitHub/source-code version	Pending
GitHub link correct and instructor-accessible	Pending
Source-code ZIP uploaded to Google Classroom	Pending
Final documentation PDF uploaded	Pending
Video or accessible link submitted	Pending
Every member has a clear voice-over segment	Pending
Screenshots, diagrams, tables and links readable	Document layout checked; missing external evidence pending
Long white folder with fastener	Pending physical preparation
All materials submitted before official deadline	Pending; confirm deadline in Google Classroom

Team Certification

We certify that the project, code, documentation, repository evidence, and video submitted for Test II represent our group’s actual work and current project status.

Team Leader Signature: _____

Date: _____

Sign after the pending submission and evidence entries have been completed and reviewed.
